


Battery Park City Update

- **BPC Ballfields Resiliency**
 - Construction Commenced: June 2021
 - Projected Completion: October 2021
- **South BPC Resiliency**
 - DEIS underway
 - Public Scoping: Fall 2021
 - 75% design Pier A Plaza/Battery; 95% design Wagner Park/MJH
 - Construction Start: Early 2022
- **North/West BPC Resiliency**
 - Consulting Engineer Project Definition Underway
 - Progressive Design-Build Contractor Selection: Early 2022

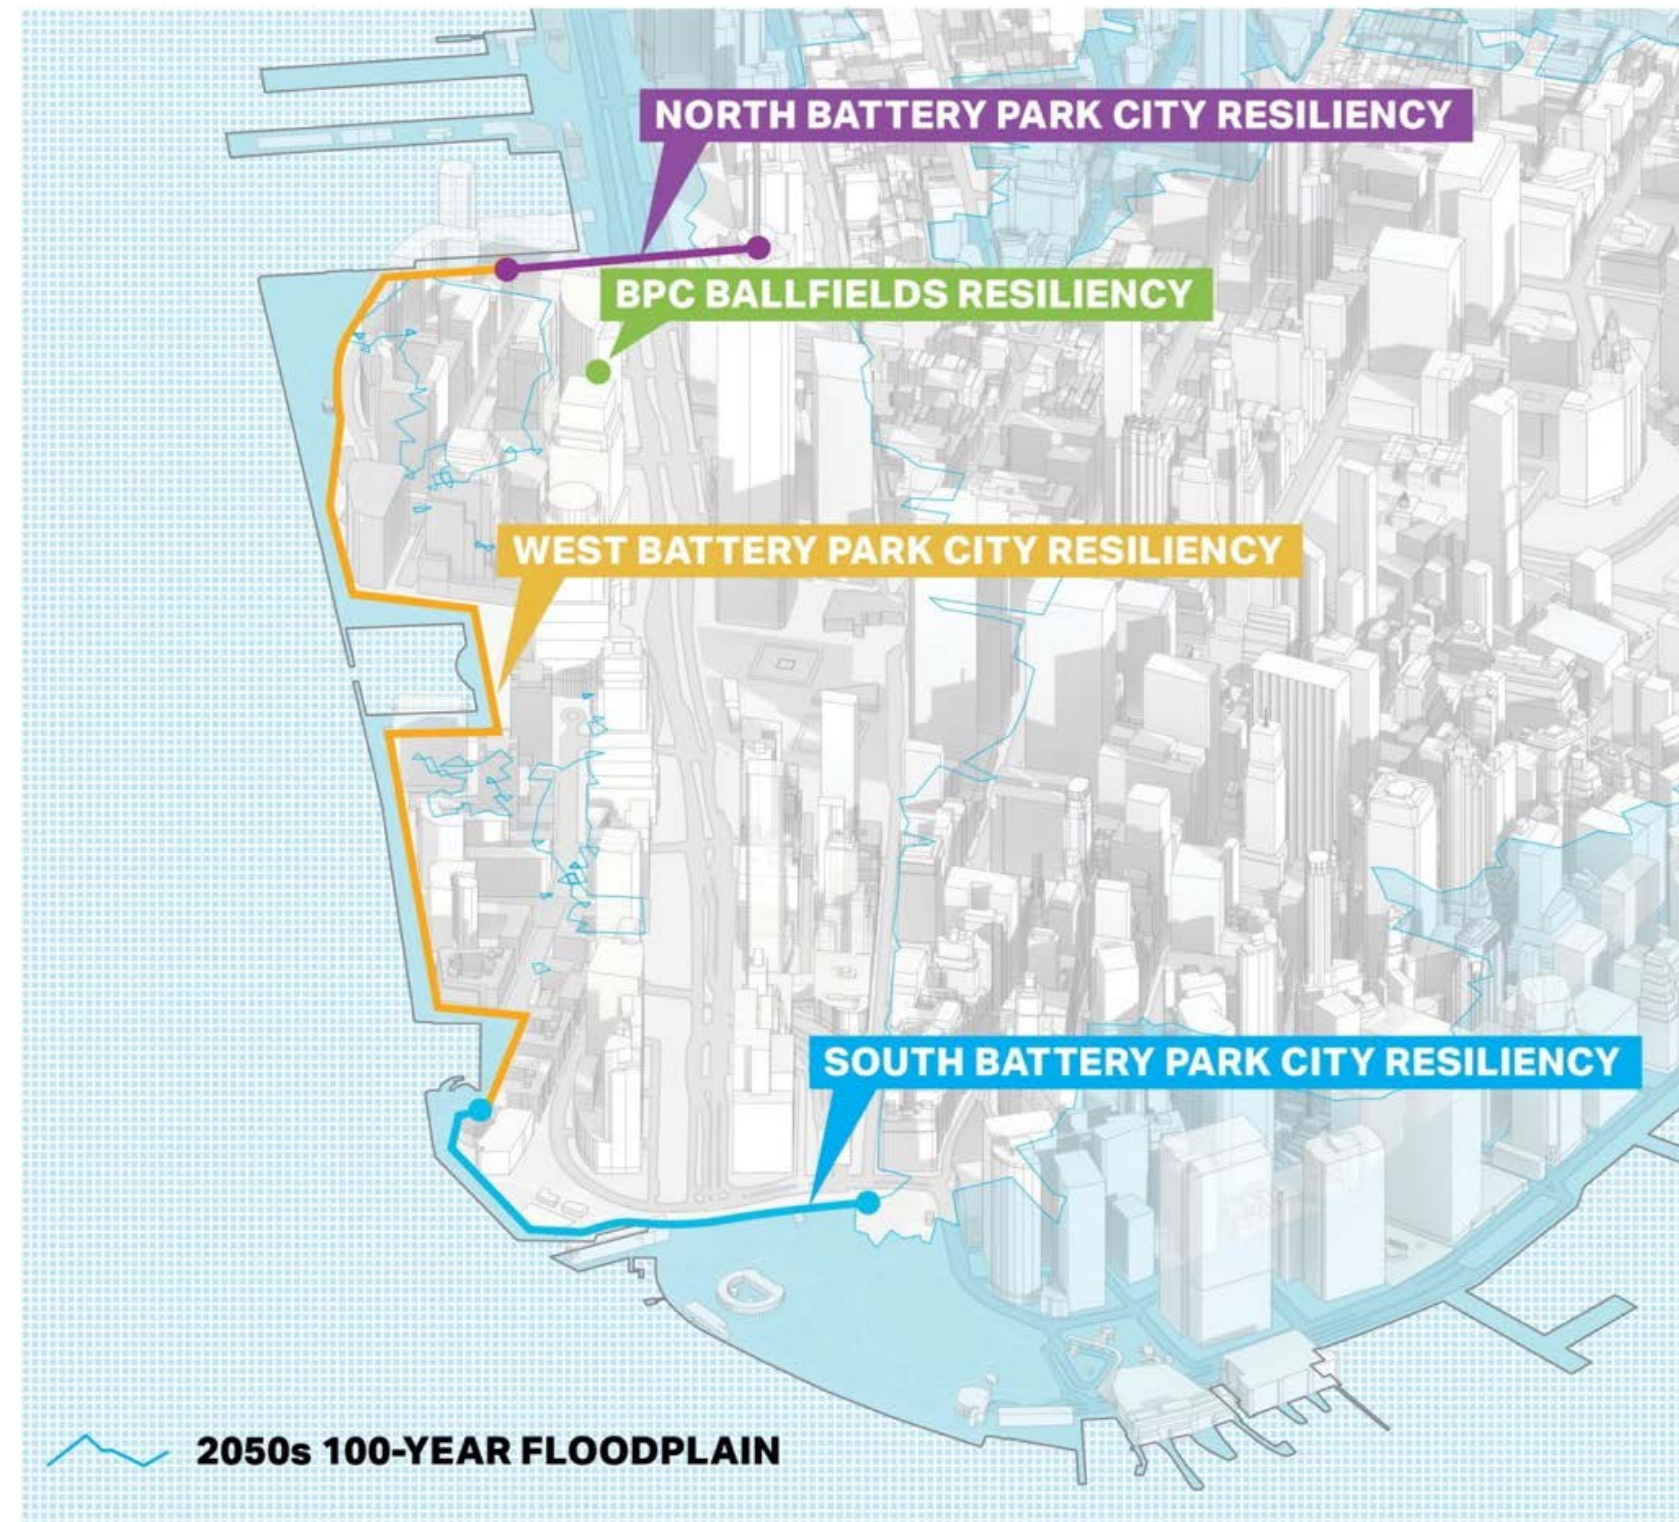

Battery Park City Update

Ballfields/Community Center Resiliency


- **Construction Commenced:** June 2021
- **Ongoing Ballfield Use Accommodated**
- **Construction Completion:** October 2021



Battery Park City Update

North/West Battery Park City Resiliency


- **Project Kickoff: June 2021**
- **Consulting Engineer Project Definition Underway (Including Public Meeting): Summer 2021**
- **PDB RFQ Issuance: Late Summer 2021**
- **PDB RFP Issuance: Late Fall 2021**
- **PDB Contractor Selection: Early 2022**

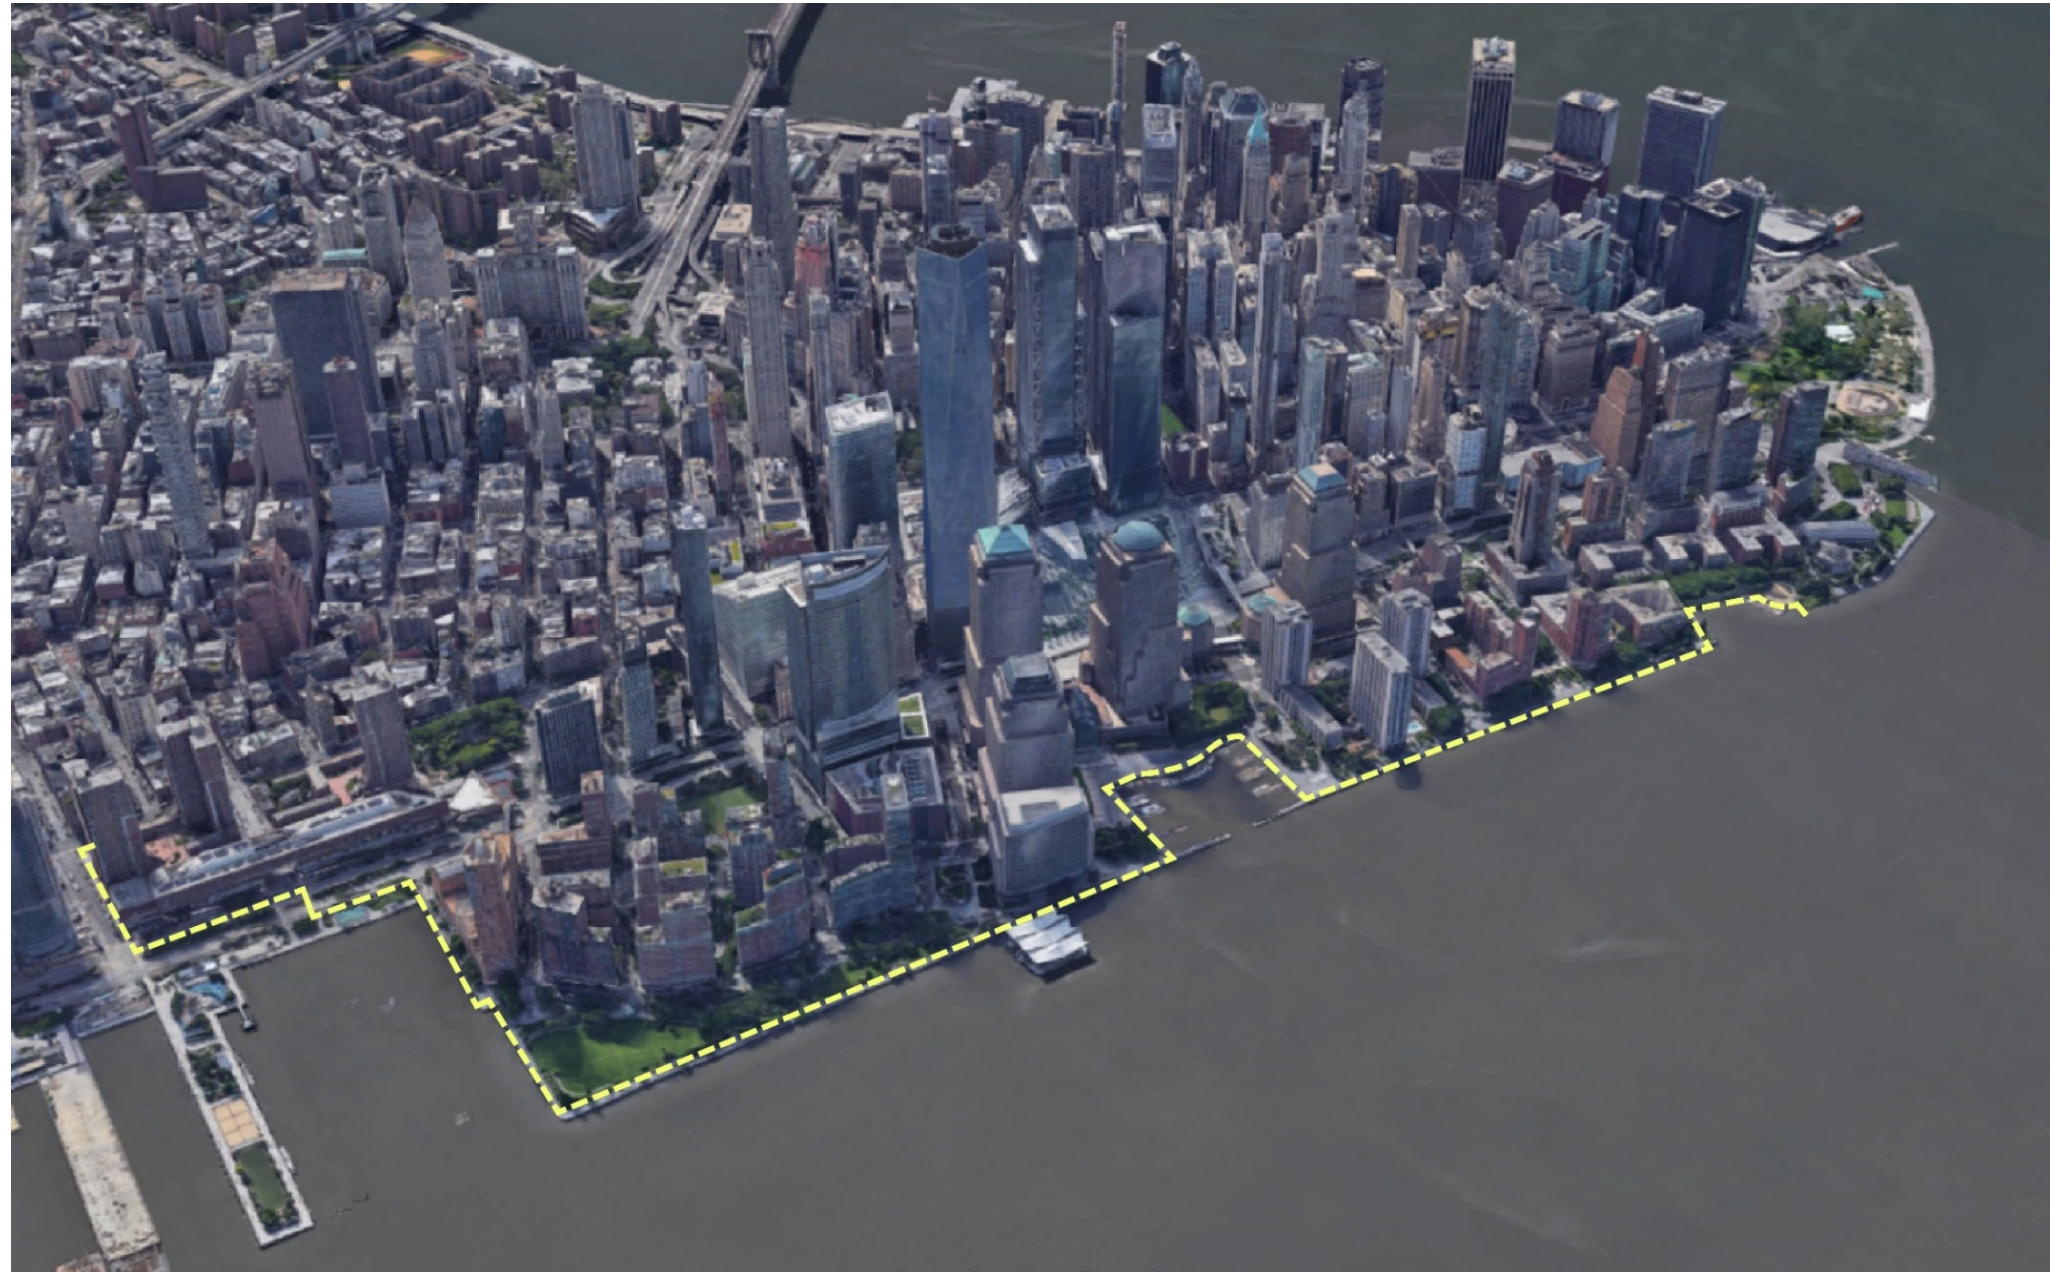

Battery Park City Update

South Battery Park City Resiliency

- DEIS in progress.
 - Public Scoping – Fall 2021
- Construction Start: Spring 2022
 - 75% design Pier A Plaza & Battery
 - 95% design Wagner Park & MJH
- Ongoing Coordination with NYCDEP Regarding Interior Drainage Design
- Final PDC Approval: Summer 2021

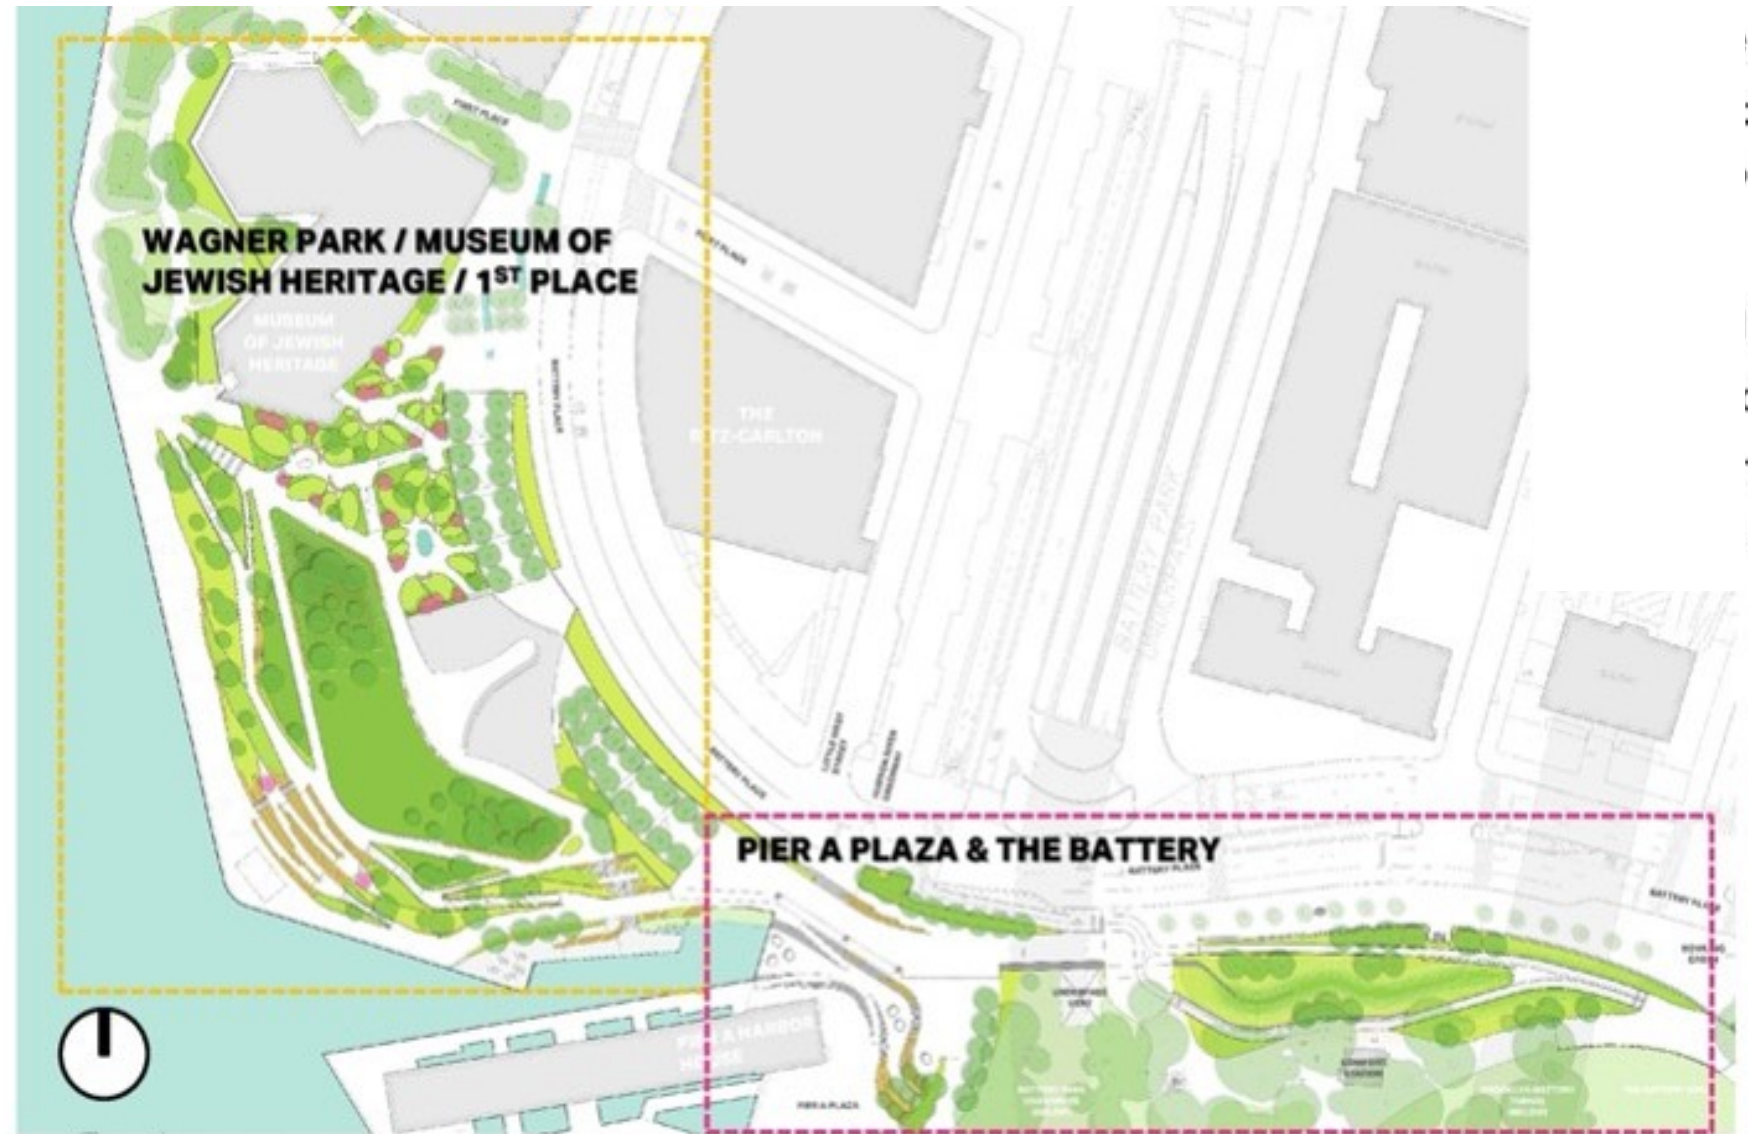


Wagner Park Pavilion Service Entrances

BATTERY PLACE DESIGN— Presented to CB 1 February 2021




BATTERY PLACE DESIGN— Presented to CB 1 – February 2021

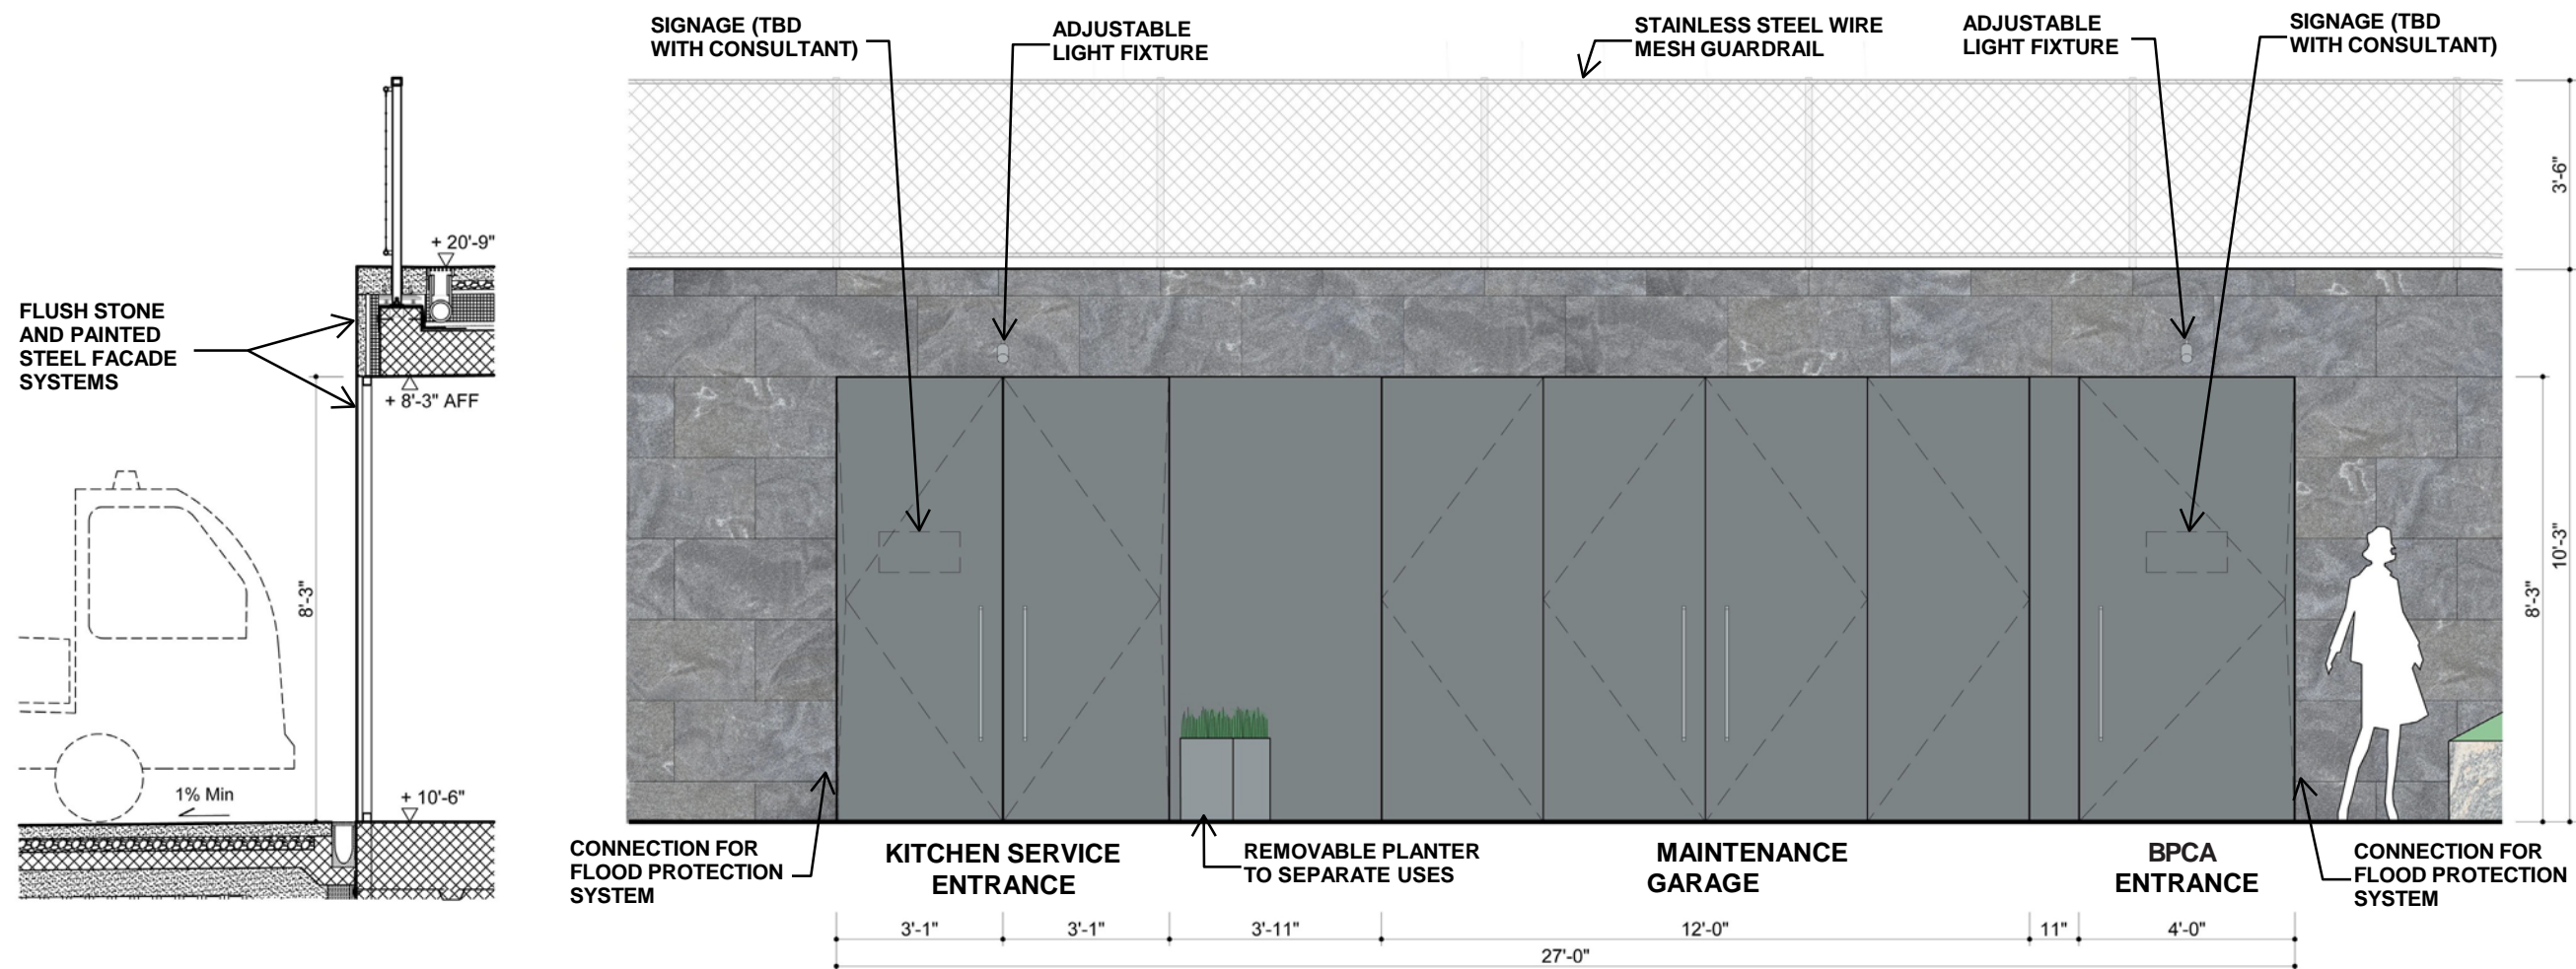


CB1 UPDATE - FEB 22

7

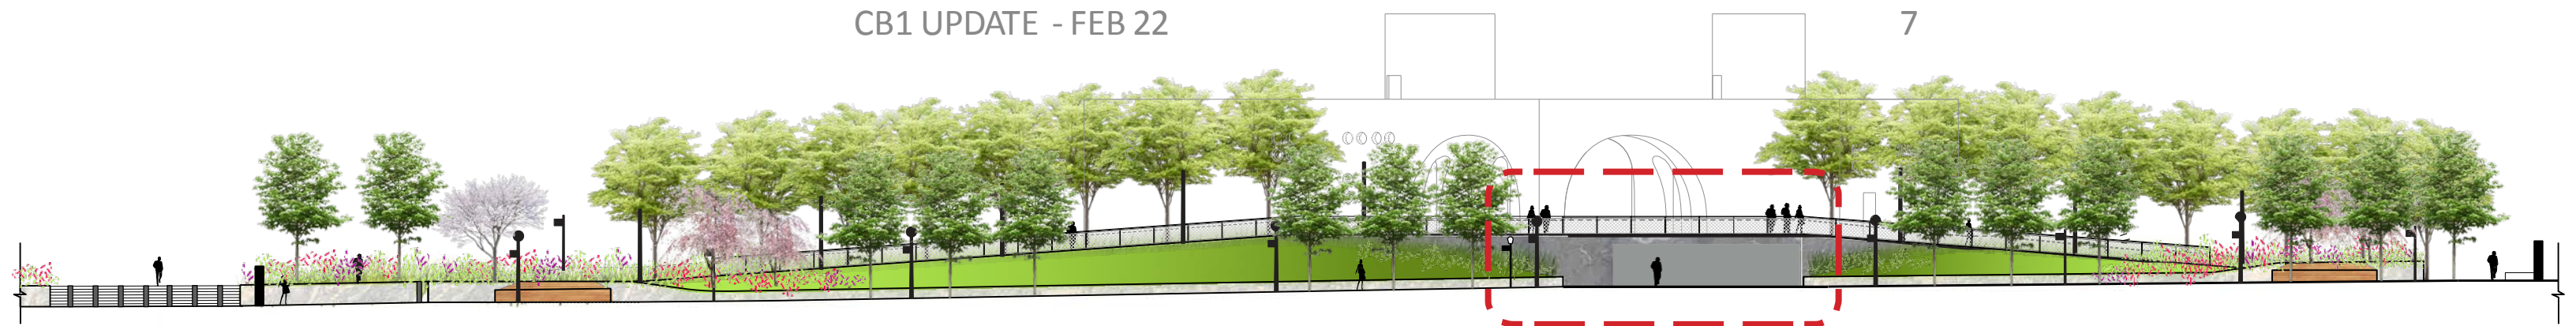

BATTERY PLACE DESIGN— Presented to CB 1 – February 2021

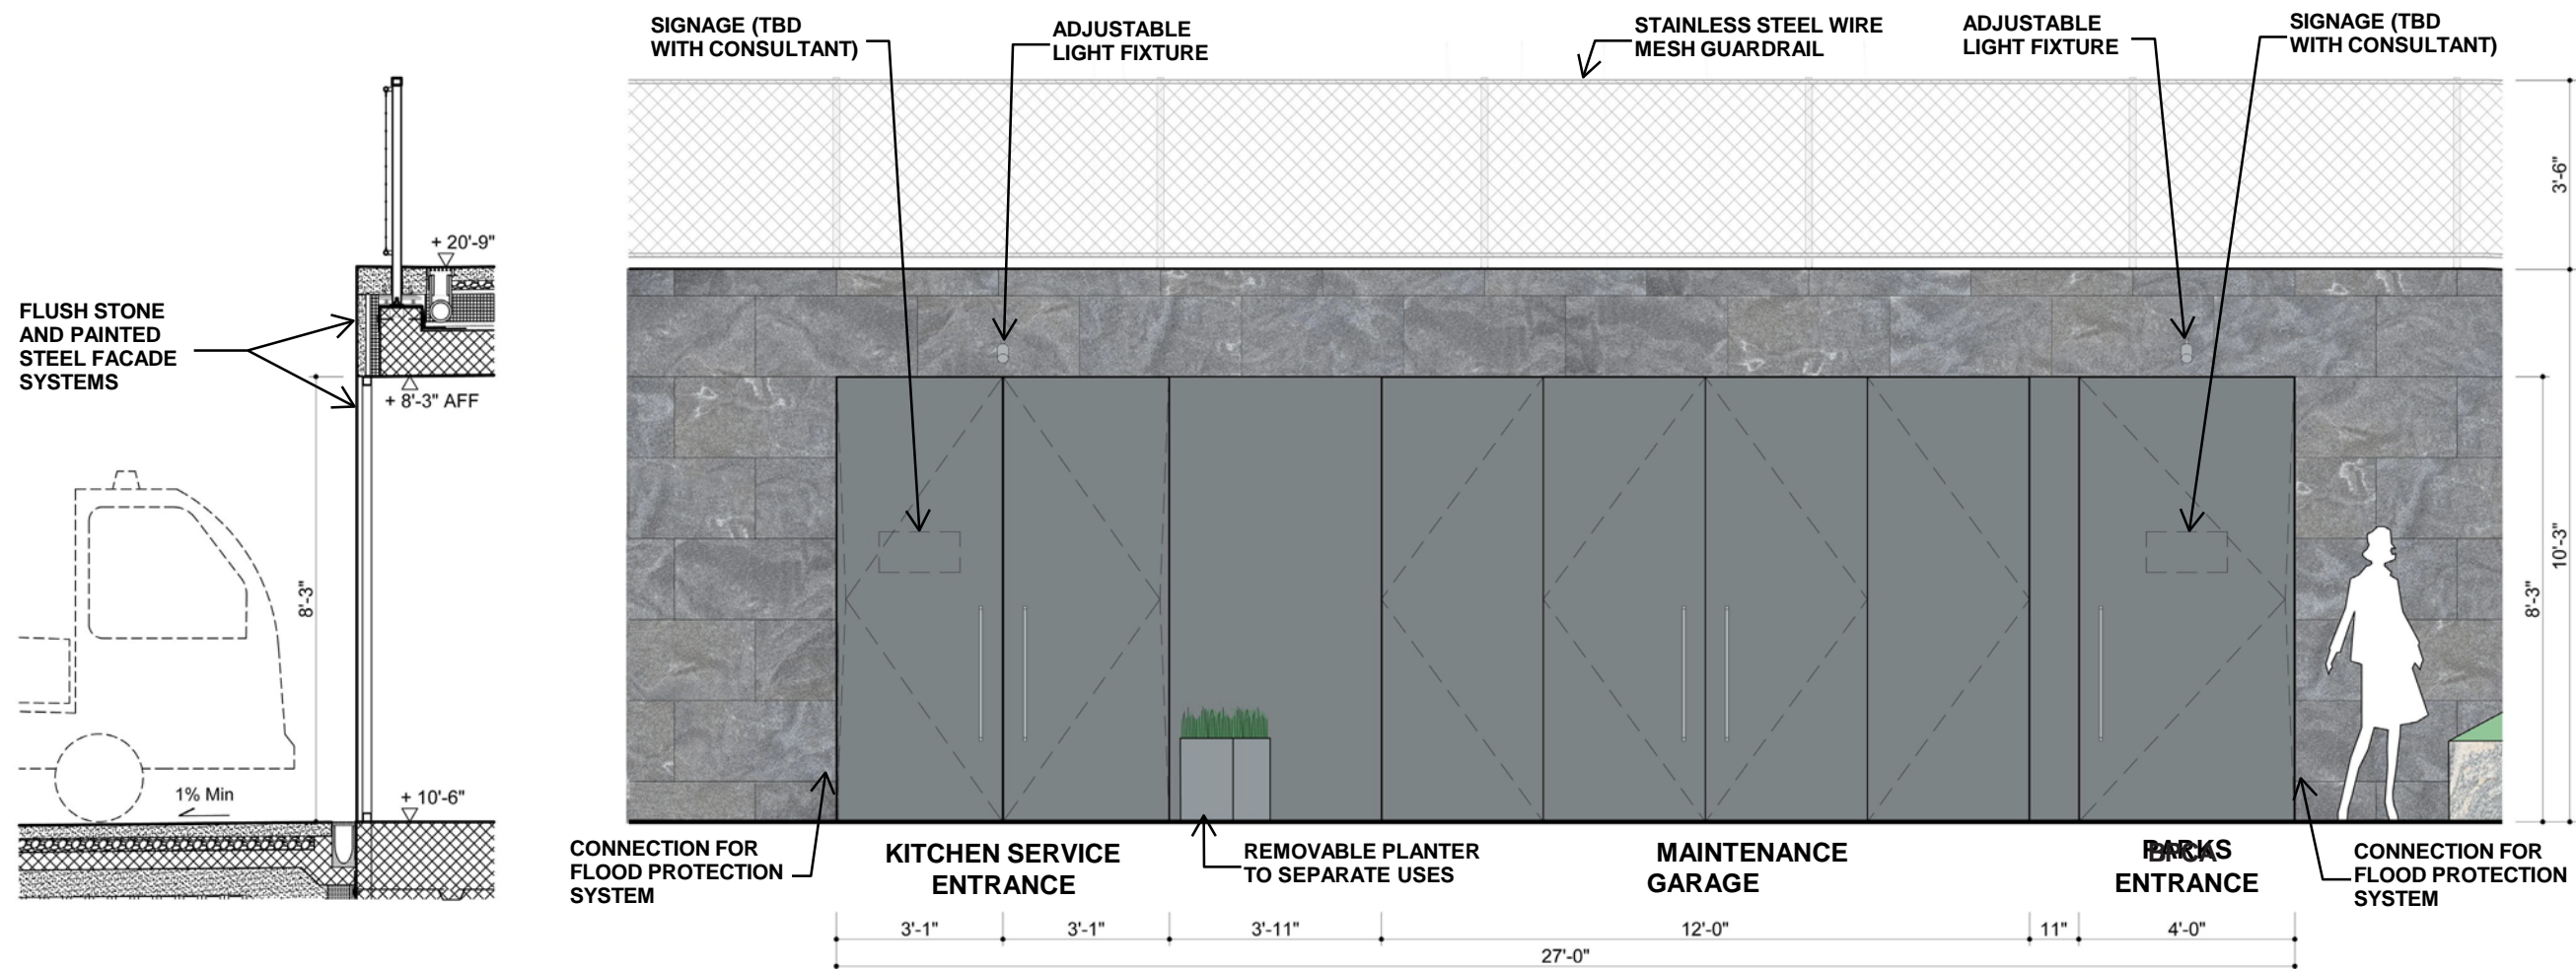

CB1 UPDATE - FEB 22



JET MIST
GRANITE



RAL 7011
PAINTED STEEL
WITH SIGNAGE (TBD)



DEPLOYABLE
FLOOD PROTECTION
SYSTEM



ADJUSTABLE
LIGHT FIXTURES





STAINLESS STEEL
WIRE DOOR PULLS



TOURNESOL RECTANGULAR PLANTERS



BATTERY PLACE DESIGN REFINEMENT– New Design Approach

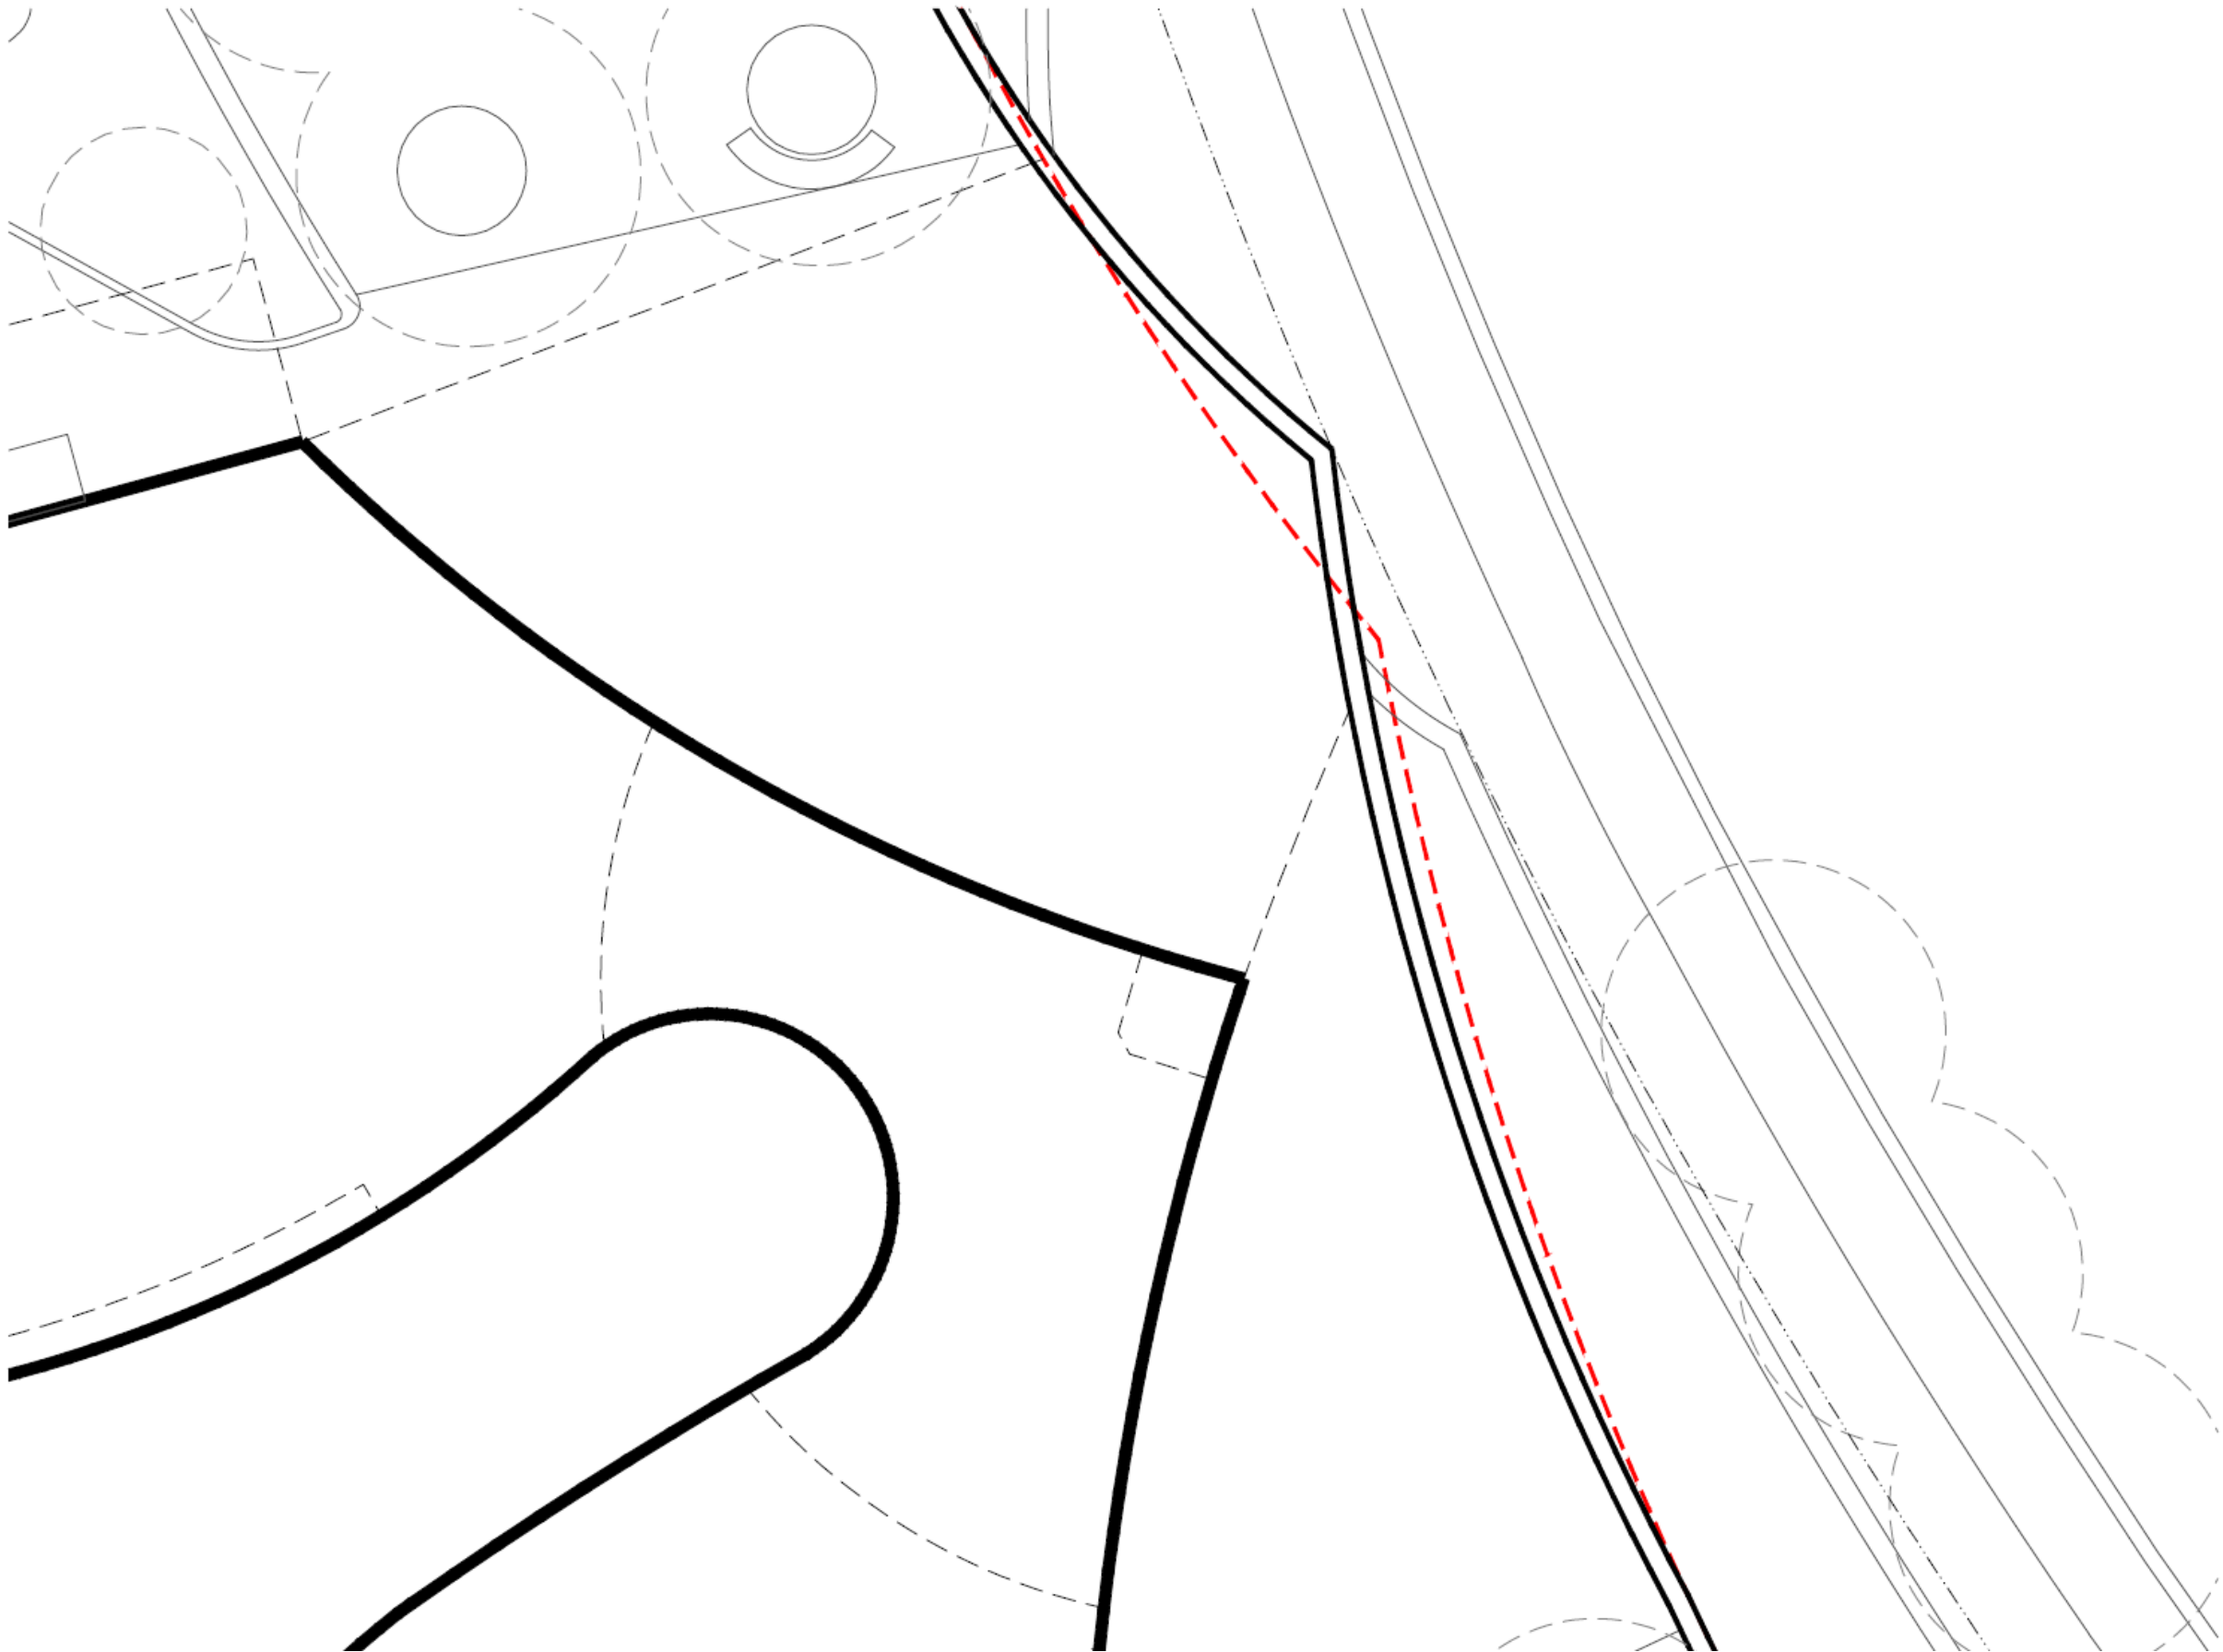


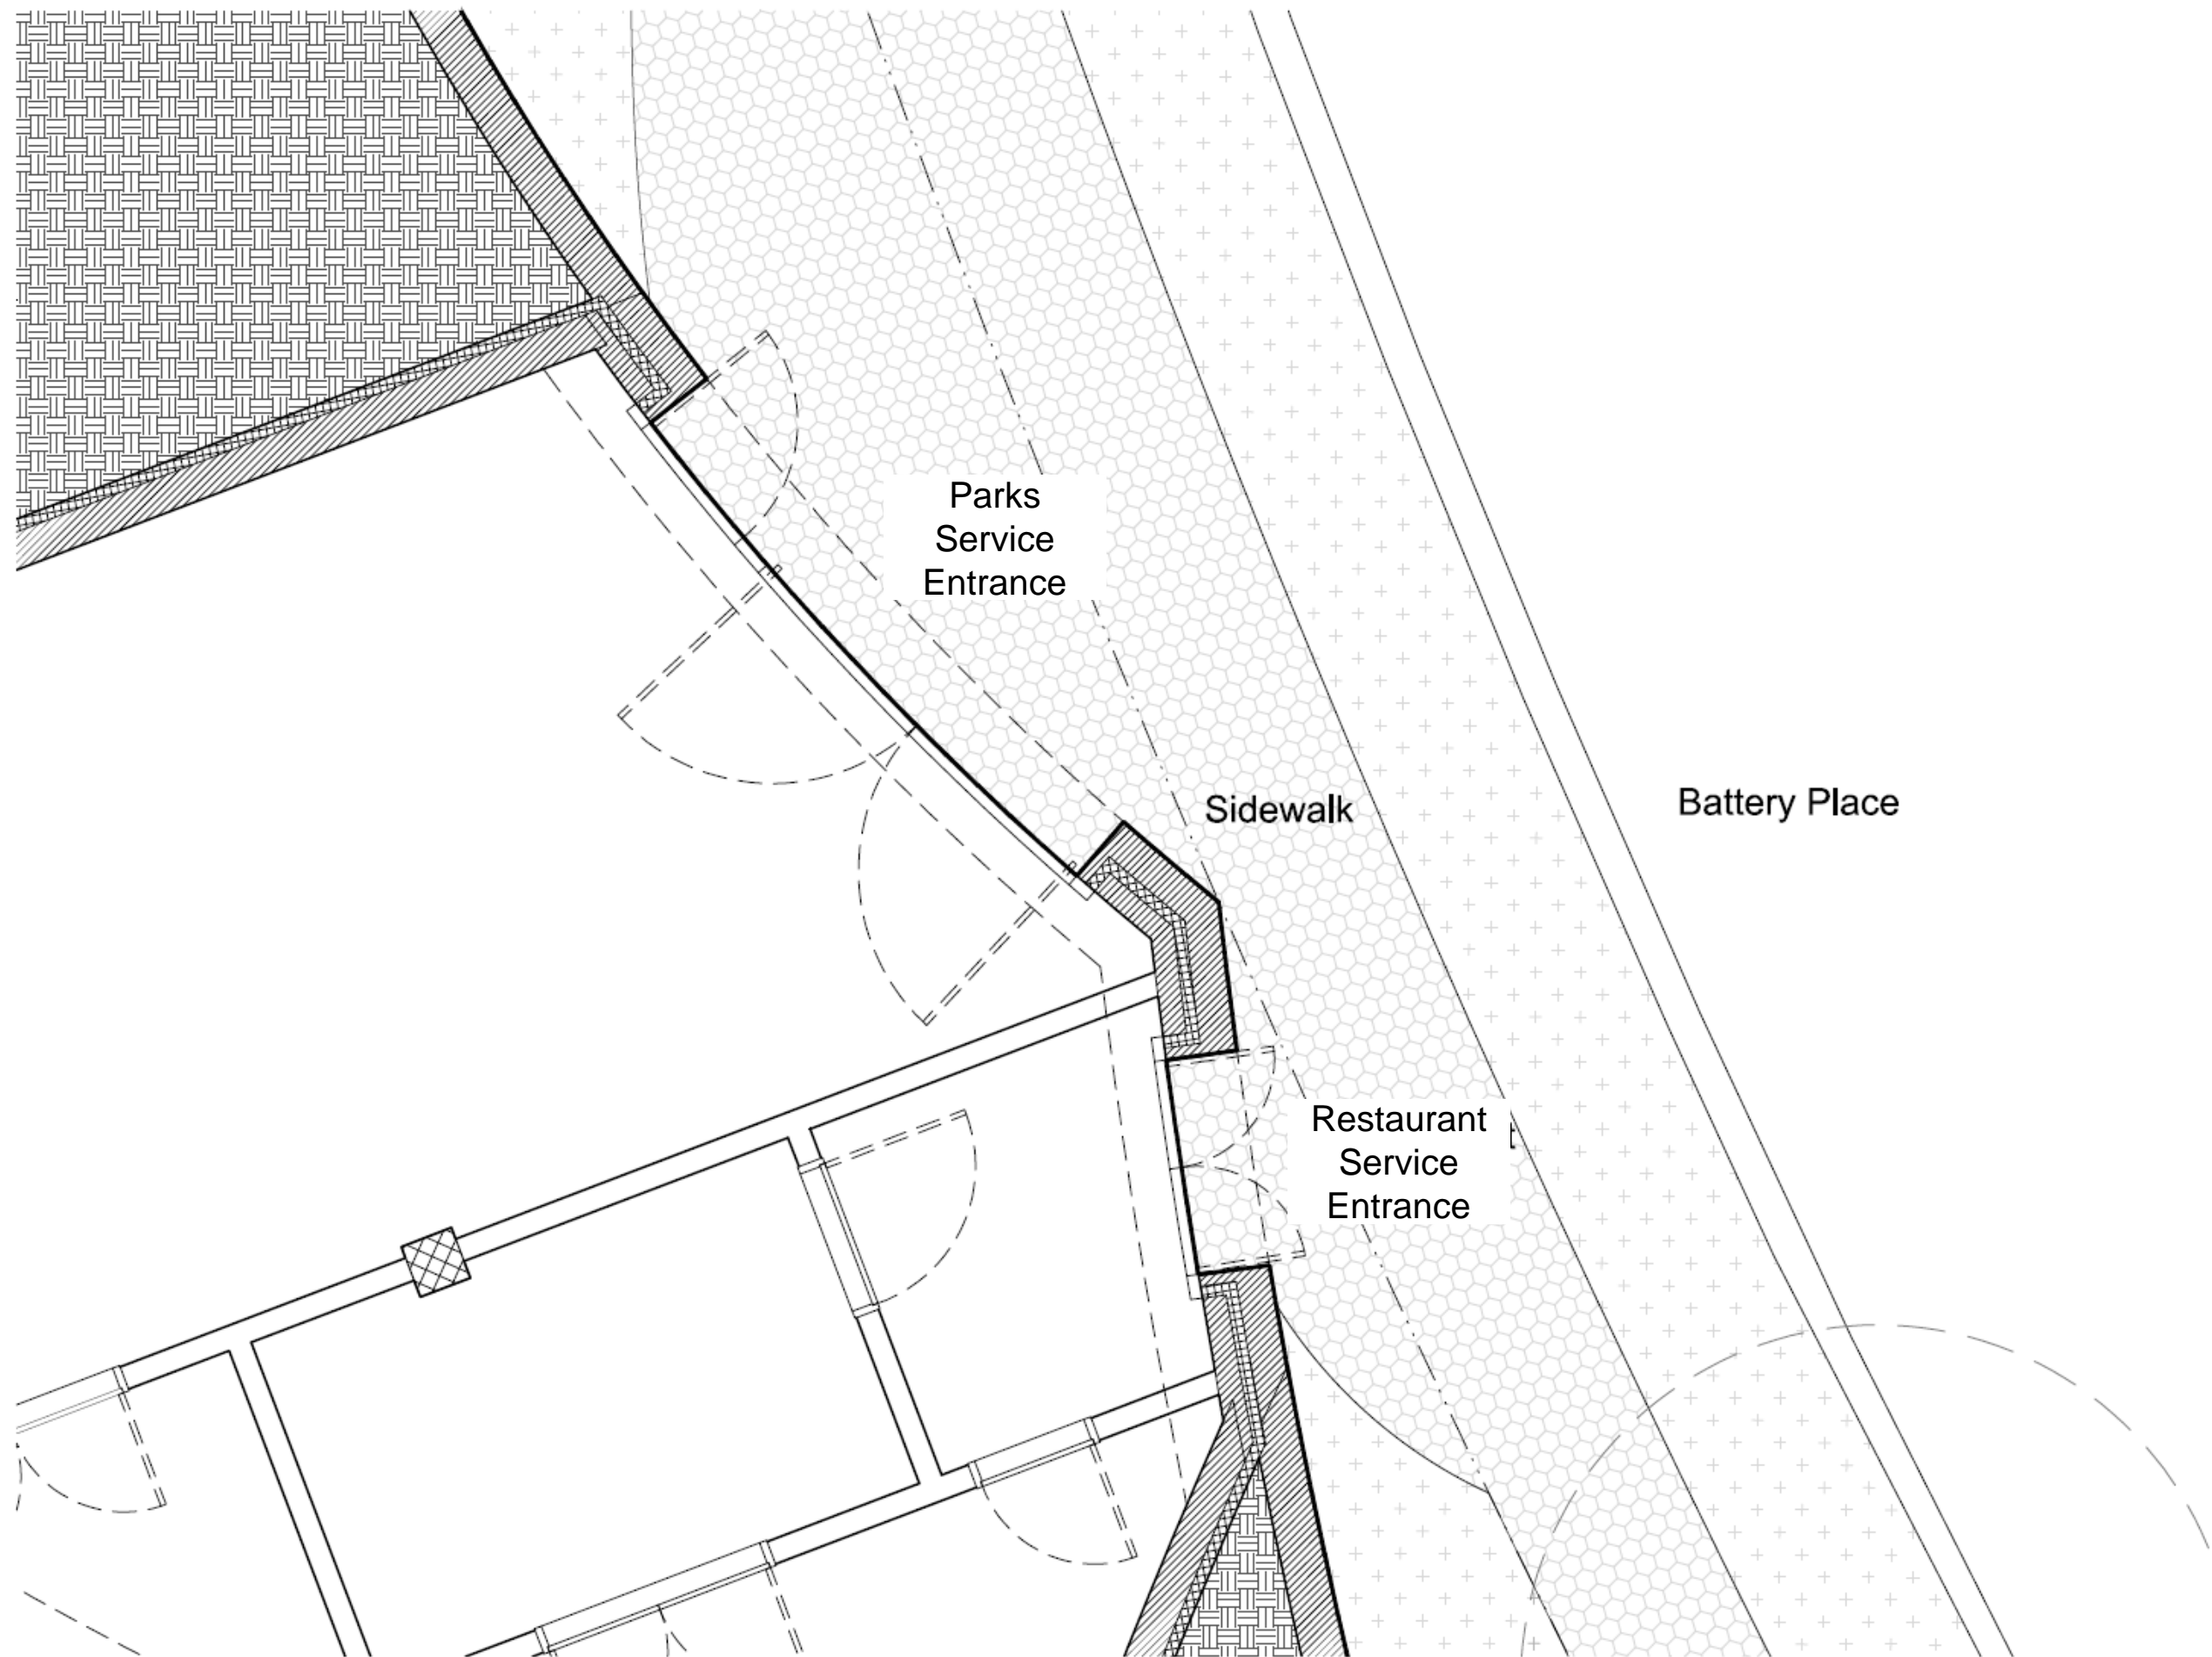





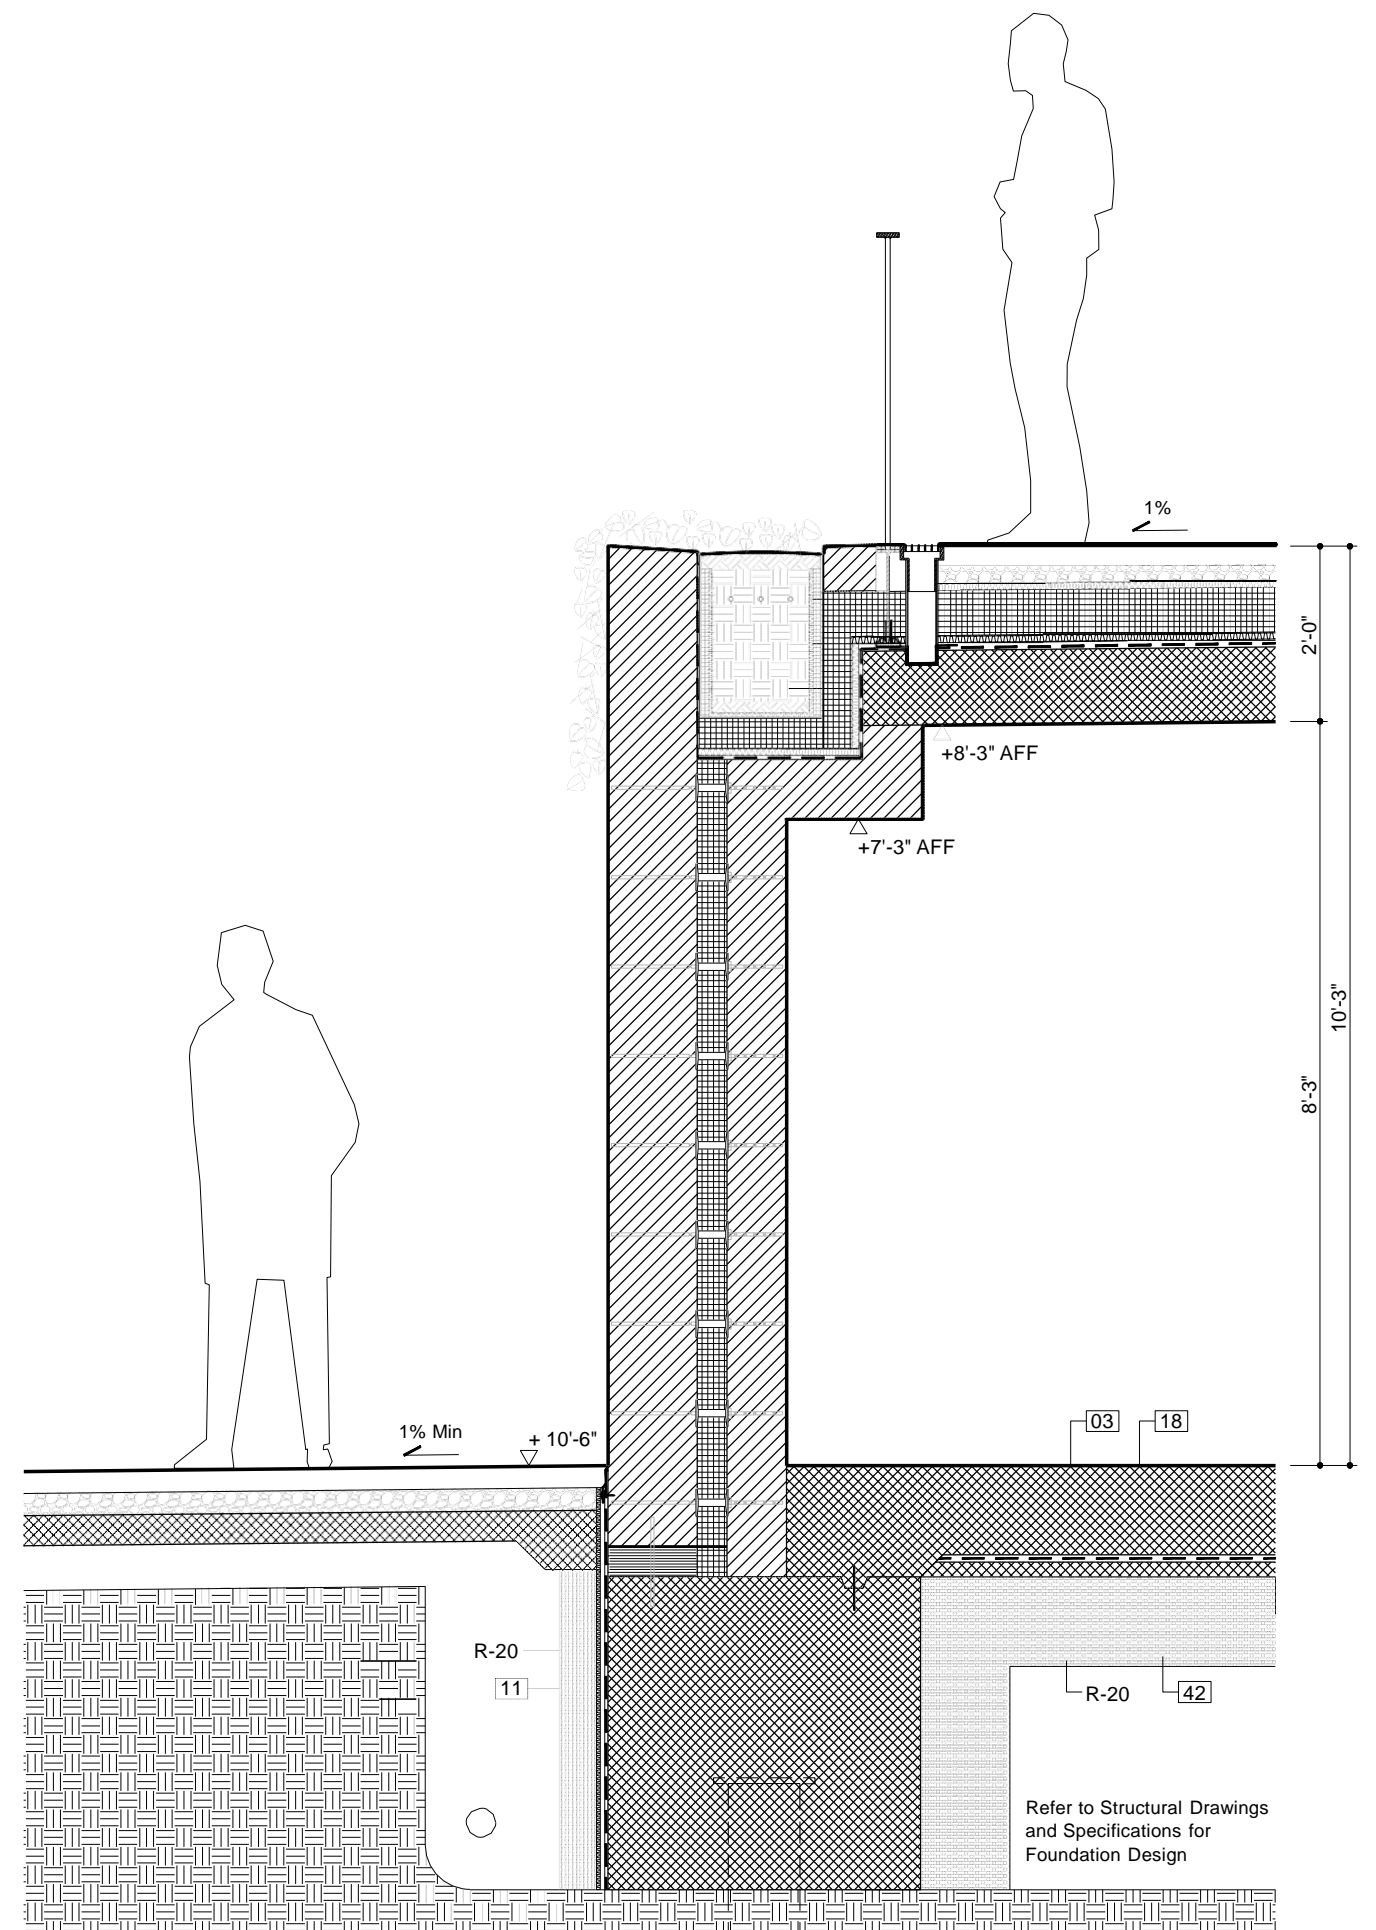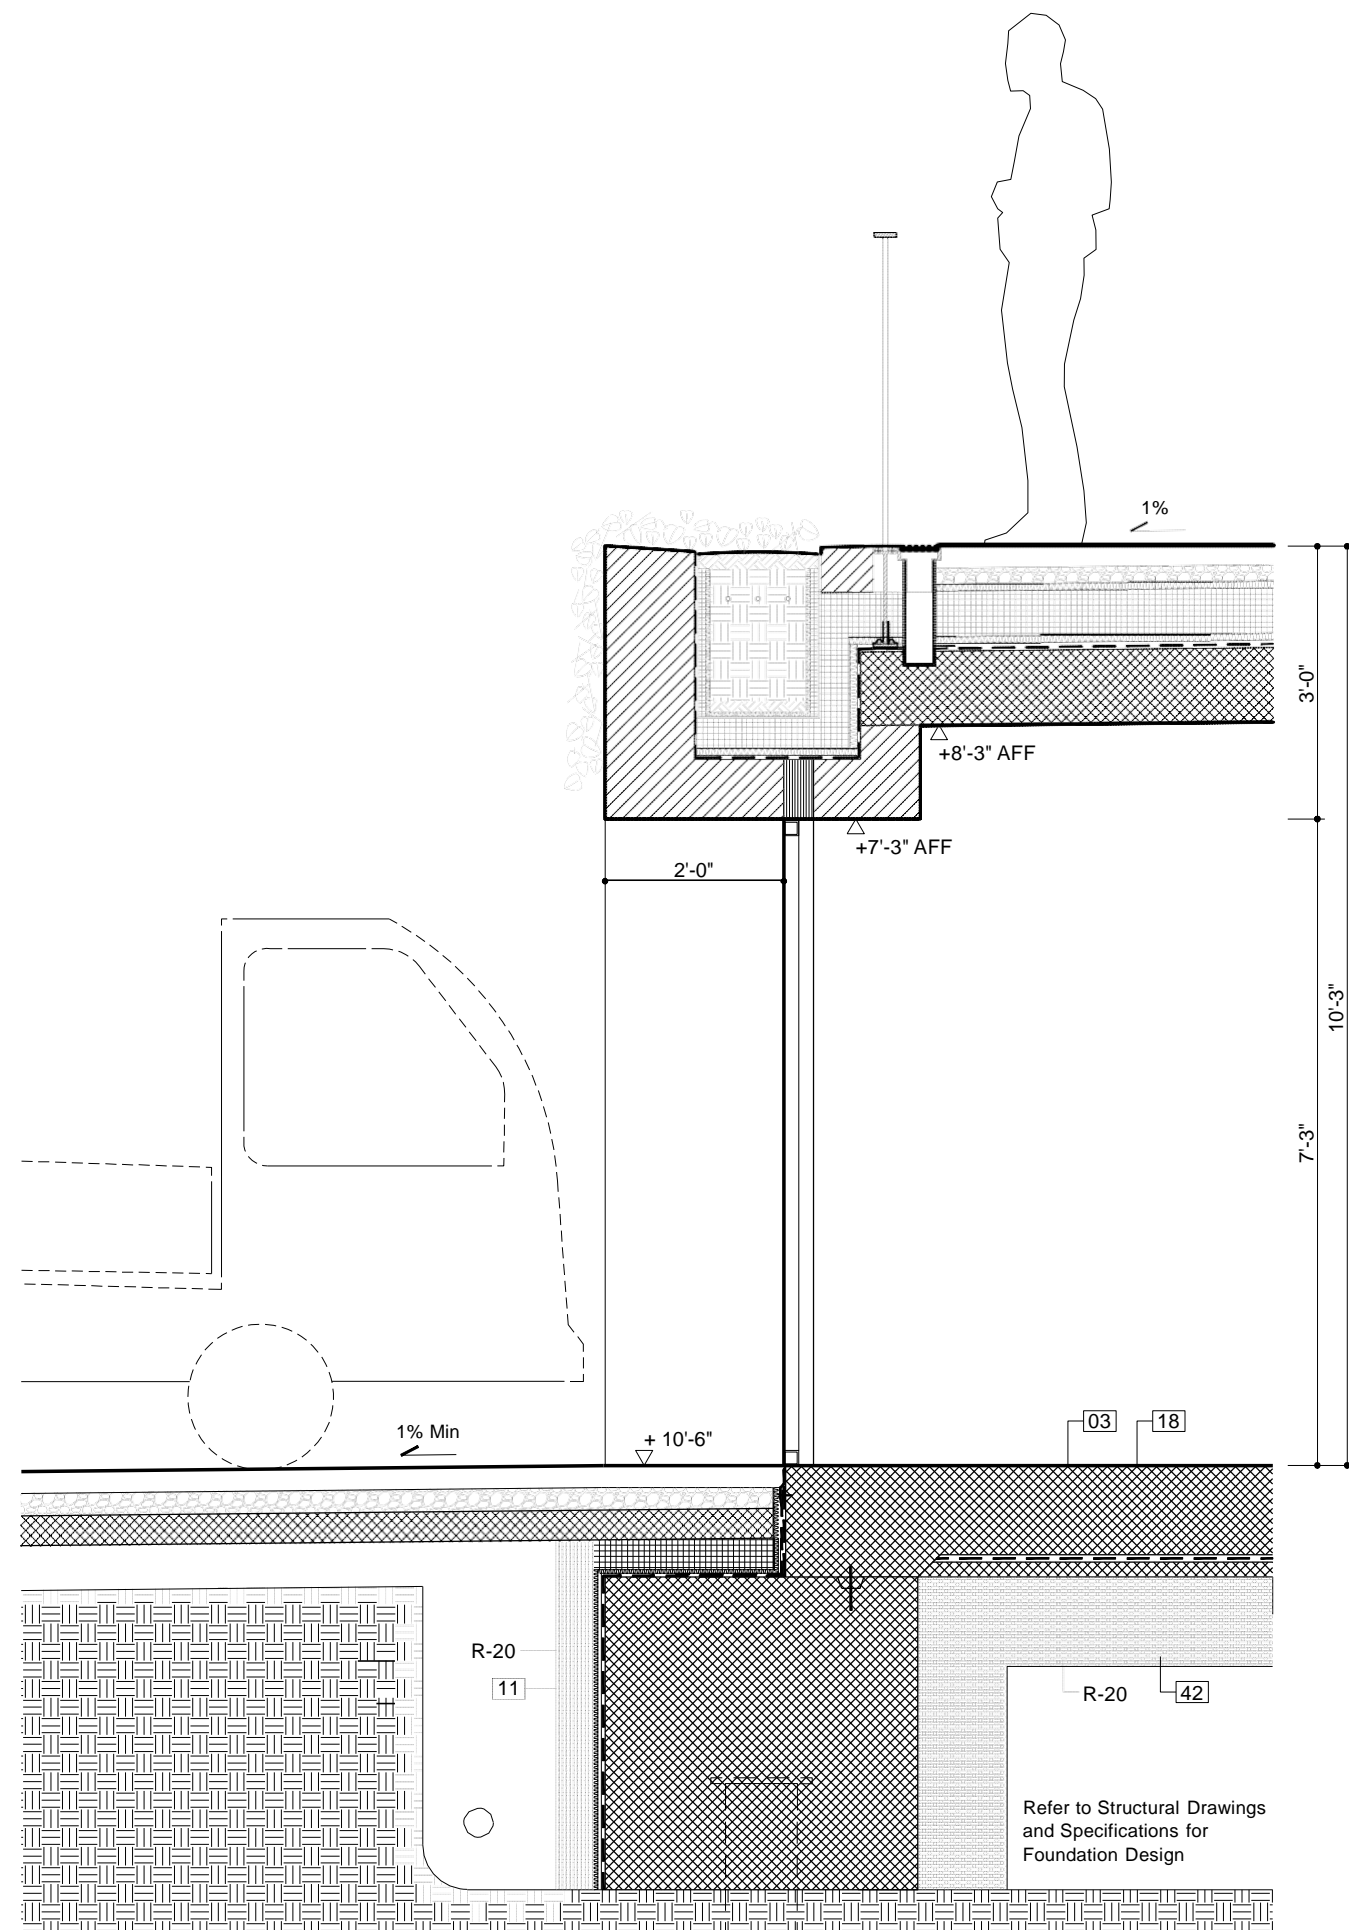


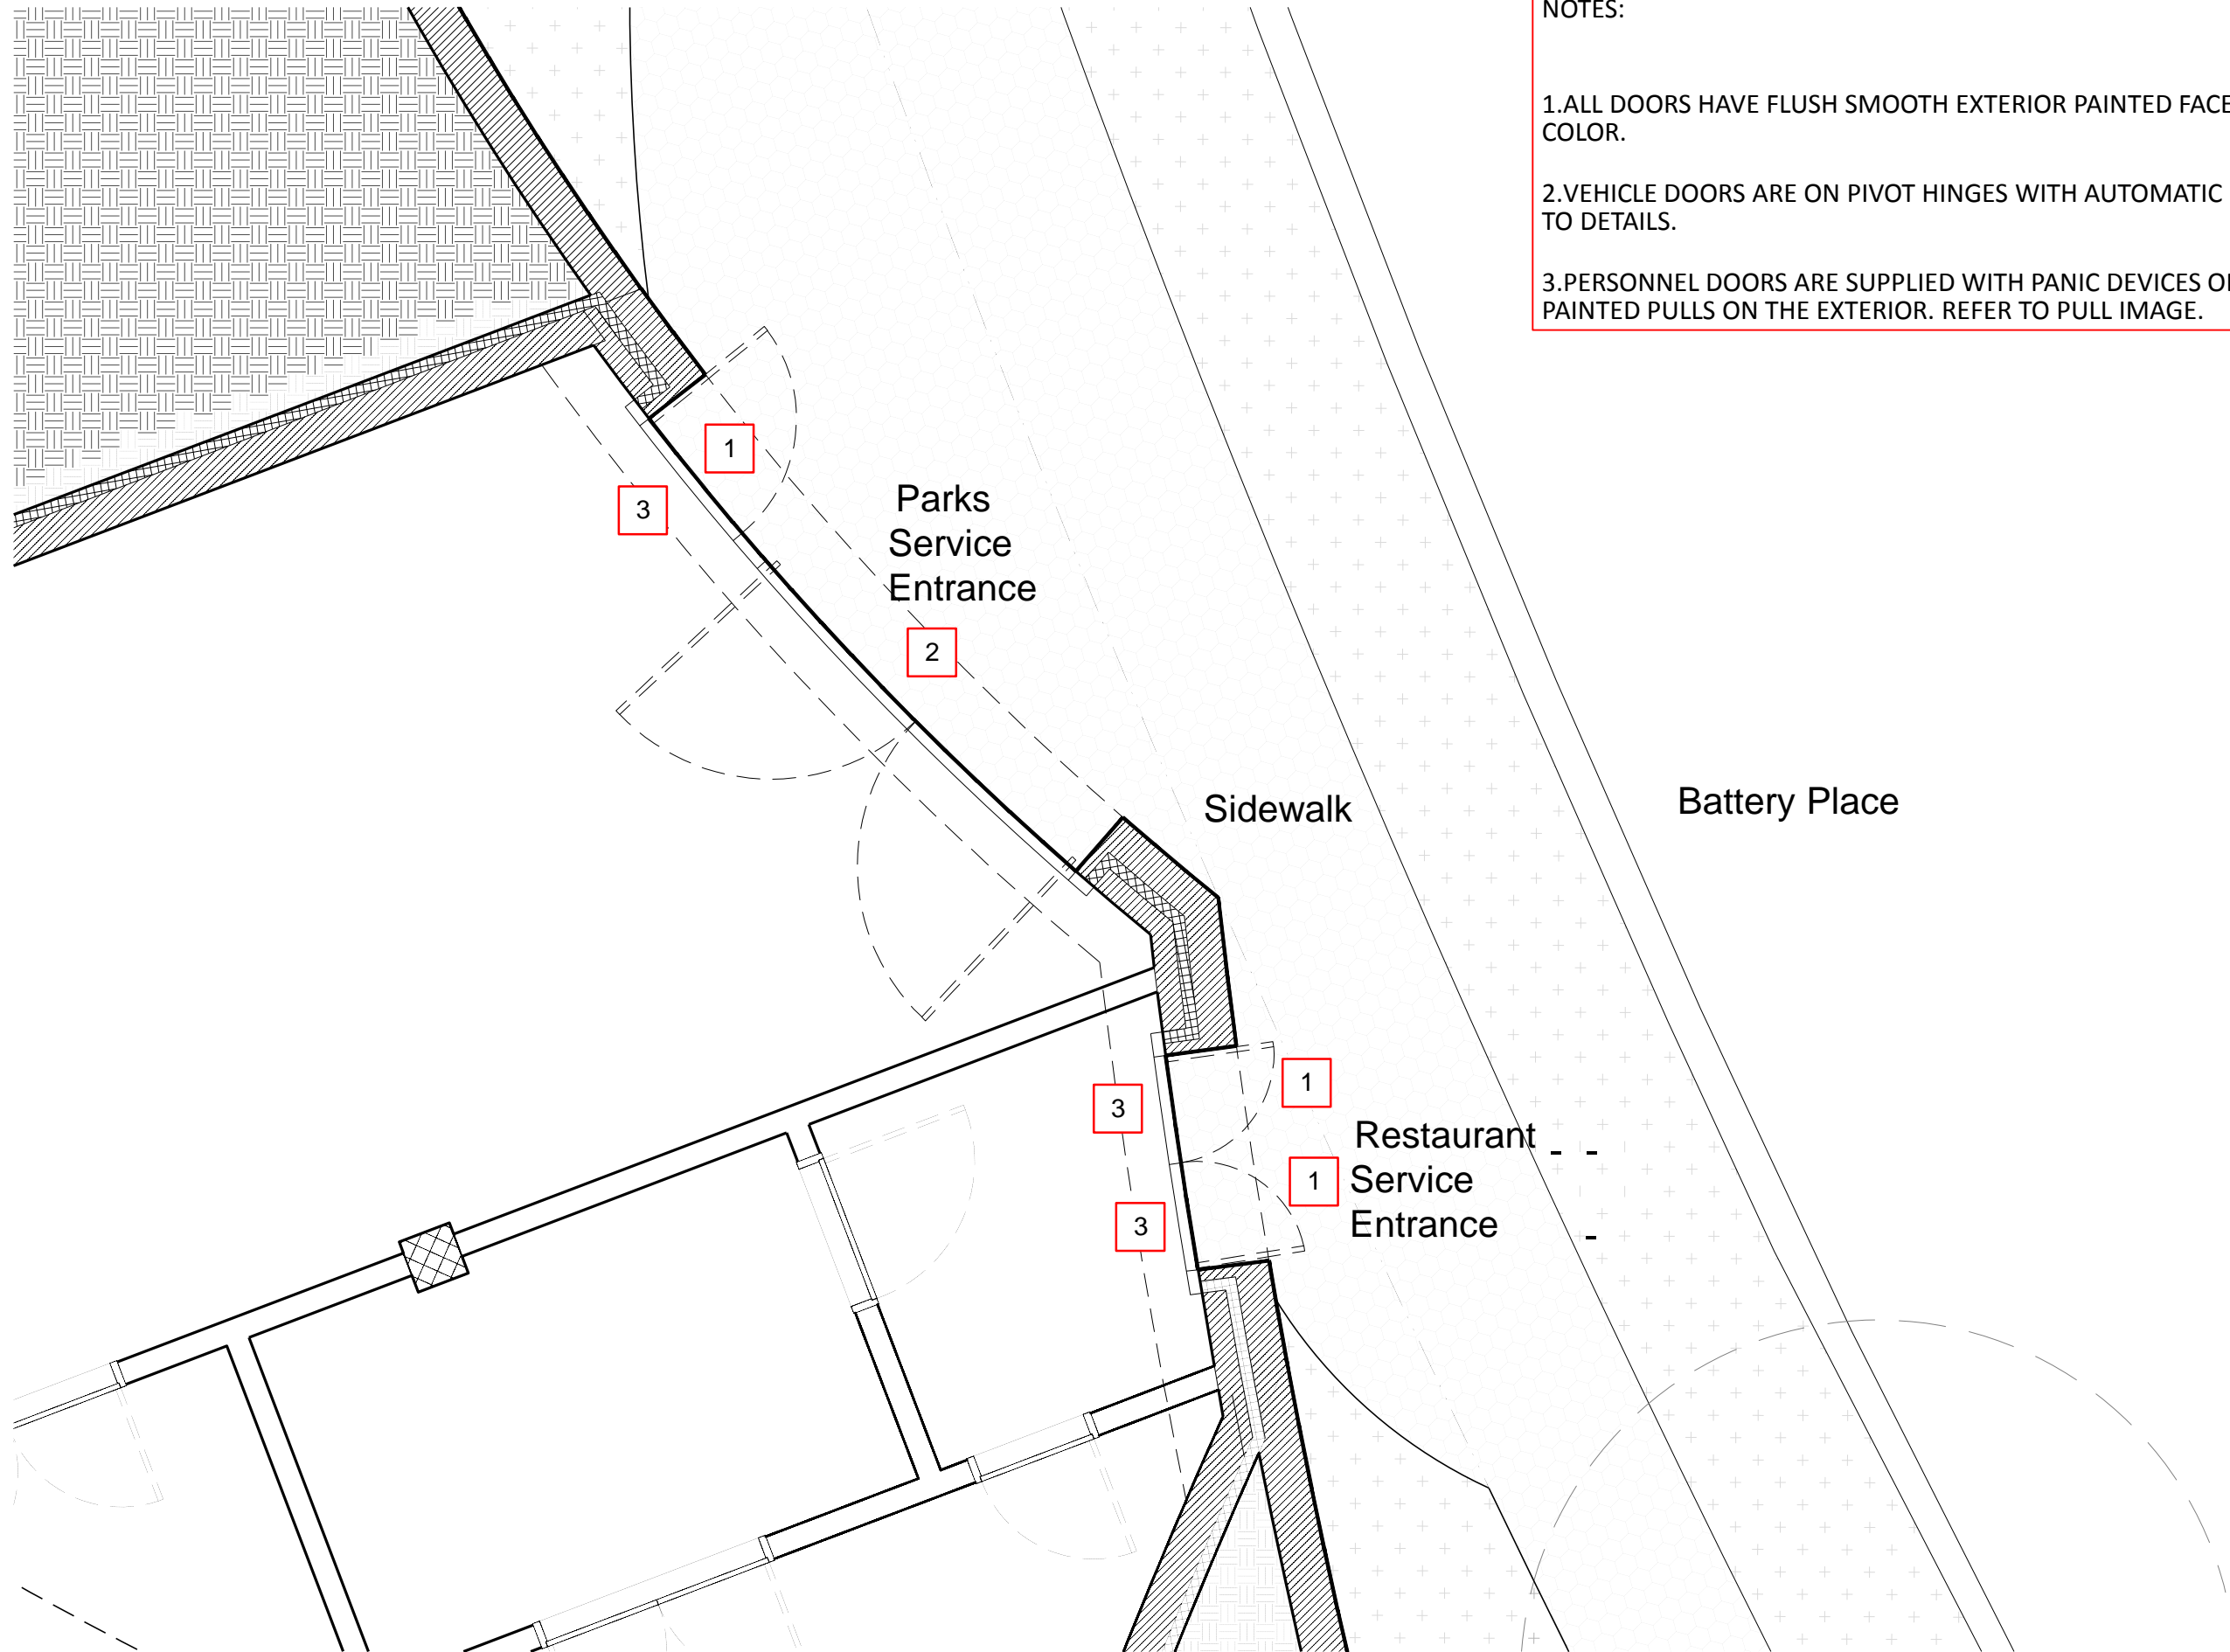

- NOTES:
- 1.ALL DOORS HAVE FLUSH SMOOTH EXTERIOR PAINTED FACES. REFER TO FINISH COLOR.
 - 2.VEHICLE DOORS ARE ON PIVOT HINGES WITH AUTOMATIC SEALS. REFER TO DETAILS.
 - 3.PERSONNEL DOORS ARE SUPPLIED WITH PANIC DEVICES ON THE INTERIOR AND PAINTED PULLS ON THE EXTERIOR. REFER TO PULL IMAGE.



Pigmented Architectural Concrete



Painted Metal Doors
RAL 030 40 30



Painted Stainless Steel Wire Door Pulls



Exterior
Park Level




Guardrail Precedent



Guardrail Precedent

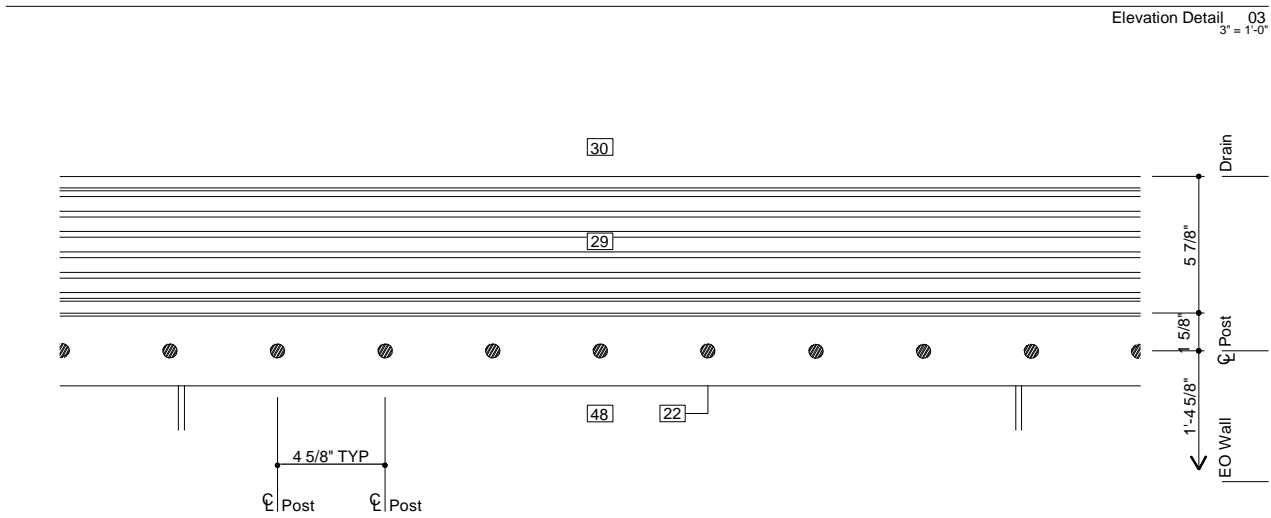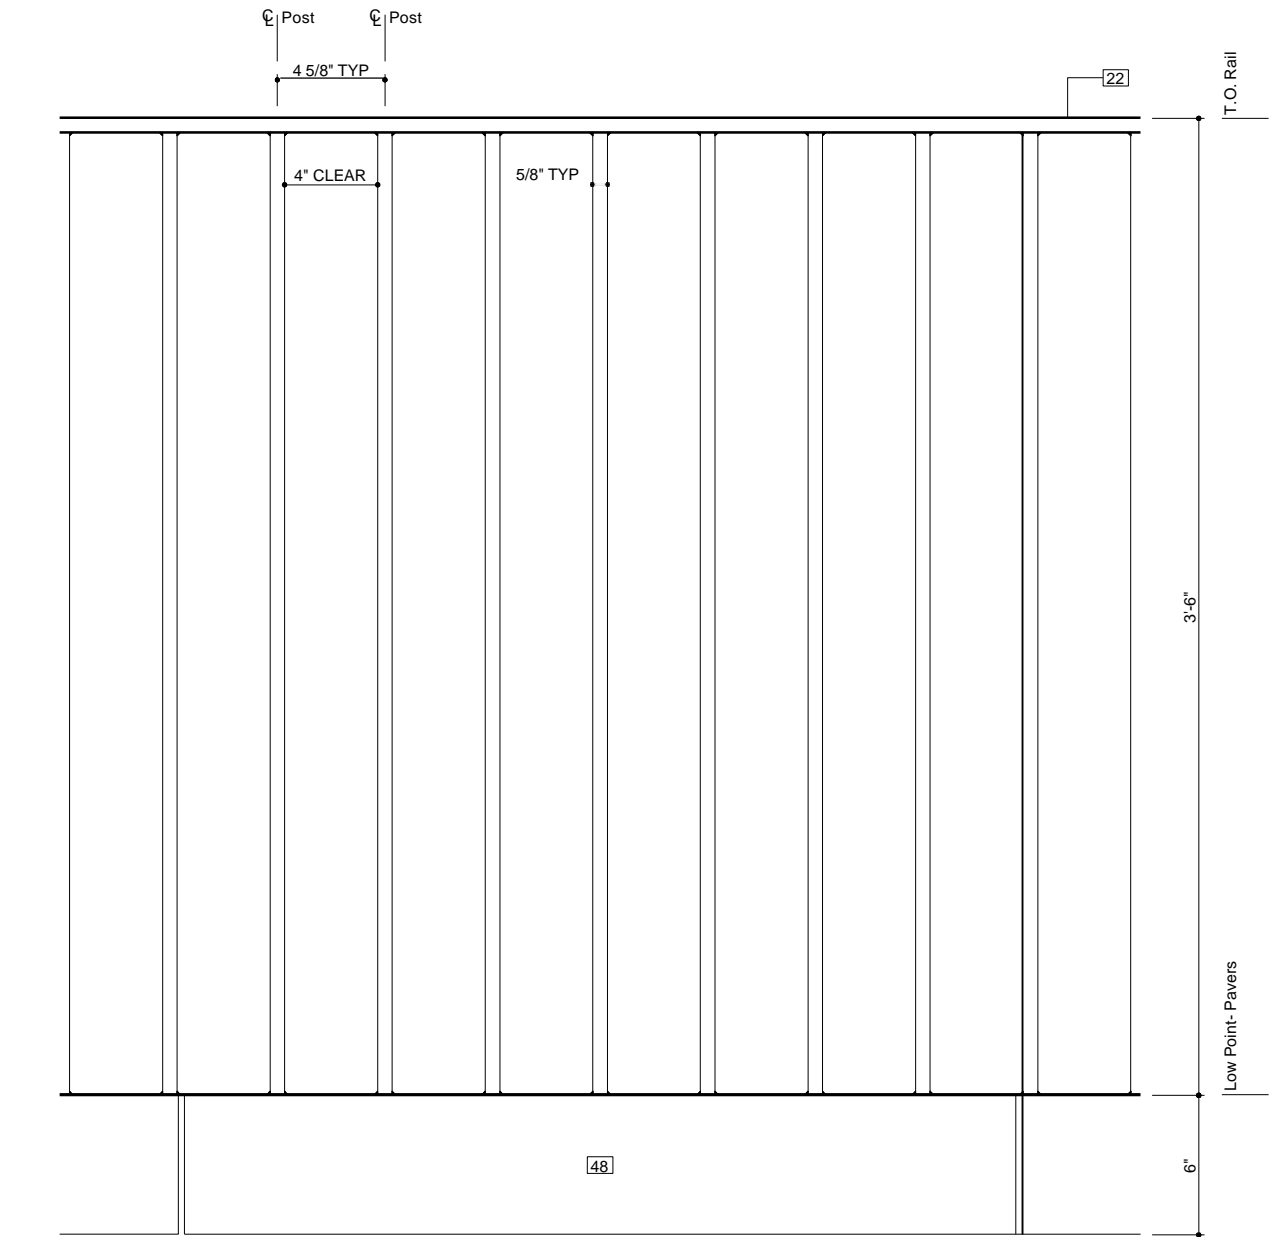

Plan Detail 02
3' = 1'-0"

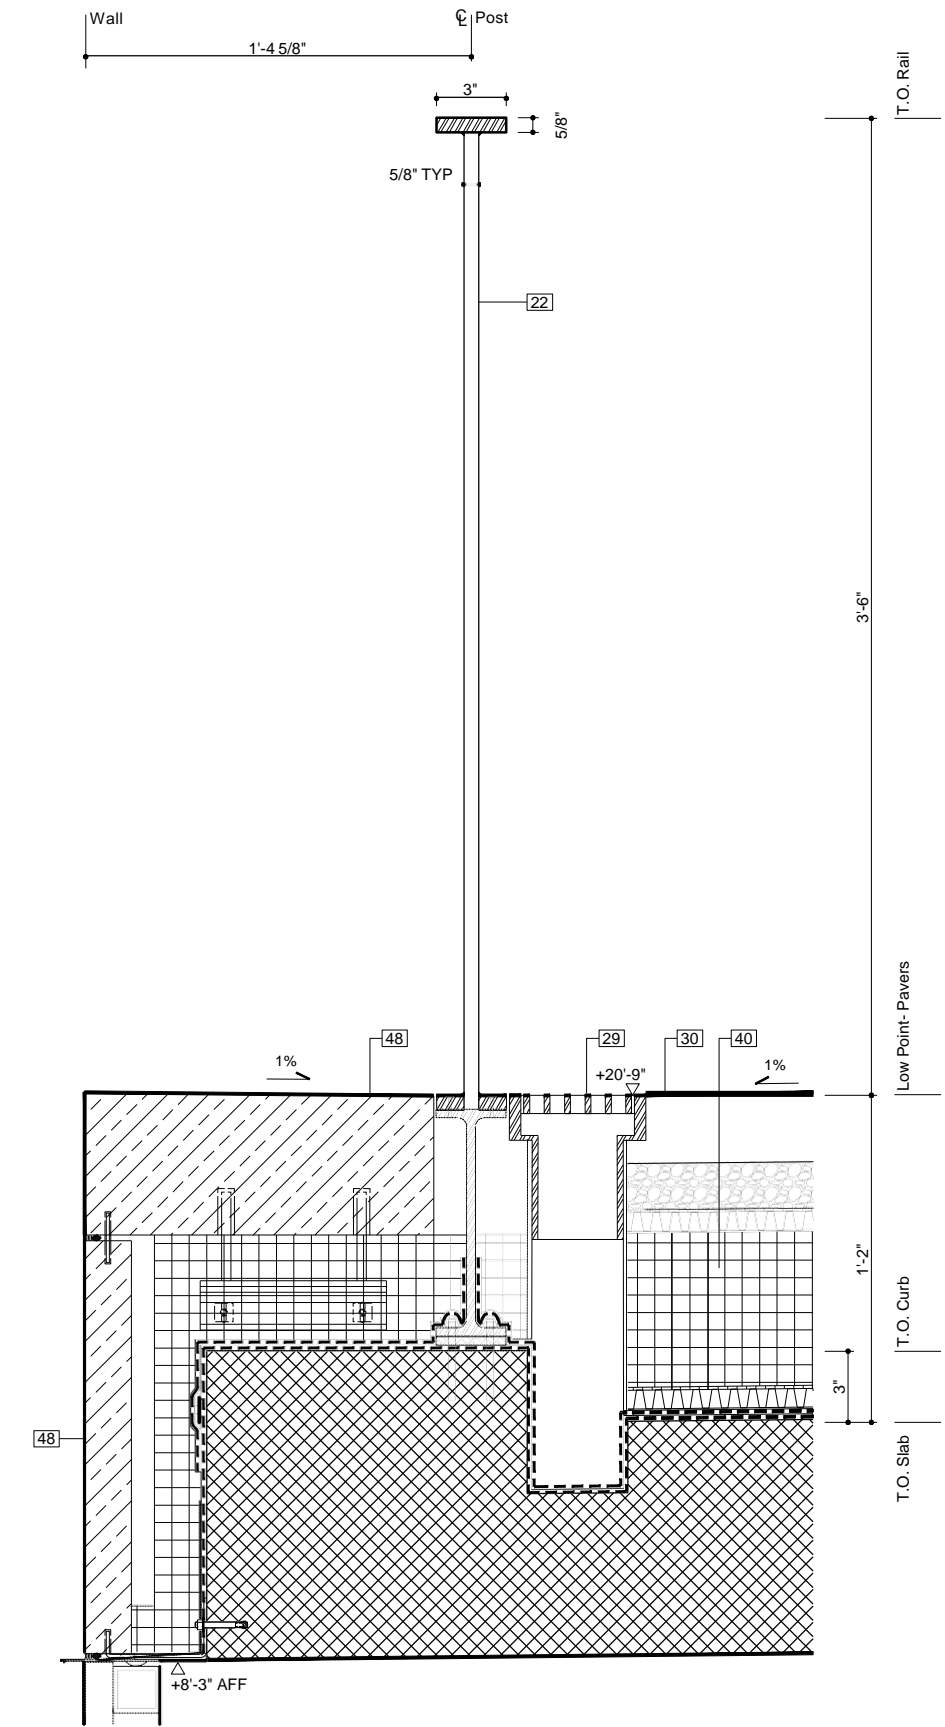

Section Detail 01
3' = 1'-0"
